

Course: Individual Software Development Process' 2026

*Iteration Report: **Iteration 1***

By **AXIS**

Chosen Irl Challenge: Project C: Department Information and Communication Hub



Jehan Tohdeng 6810545514

Thanakorn Innok 6810545620

Piyatida Muanjaingam 6810545760

Ratamon Charoenratanakun 6810545883


Table of Contents

1. Project Snapshot.....	1
1.1 Project-Wide Gantt Chart.....	1
1.2 Current Iteration Gantt Chart.....	2
2. Sprint/Board Status Snapshot.....	3
3. Scope Addition/Change Log.....	4
4. Retrospective.....	4
5. Testing & Quality Notes.....	5
6. Project Risk Register.....	6
7. Individual Contribution Log.....	7

1. Project Snapshot

Project Repository: <https://github.com/ratamon2606-create/AXIS>


1.1 Project-Wide Gantt Chart

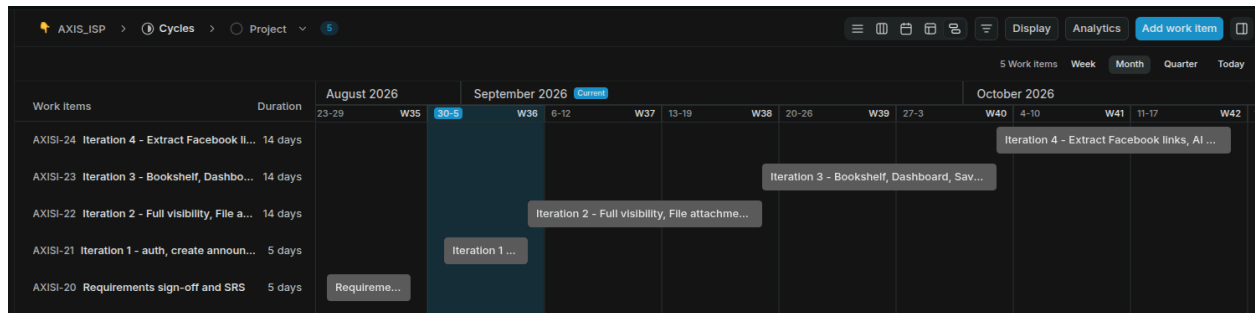

Critical Path: Requirements sign-off → Authentication and role model → Content model and database schema → Create and edit content item (US-5) → Thread and follow-up posts → Feed with visibility rules (US-1) → Search and the expiry lifecycle → Facebook retrieval and assisted field entry → Deployment

Critical Path Duration: 98 calendar days

1.2 Current Iteration Gantt Chart

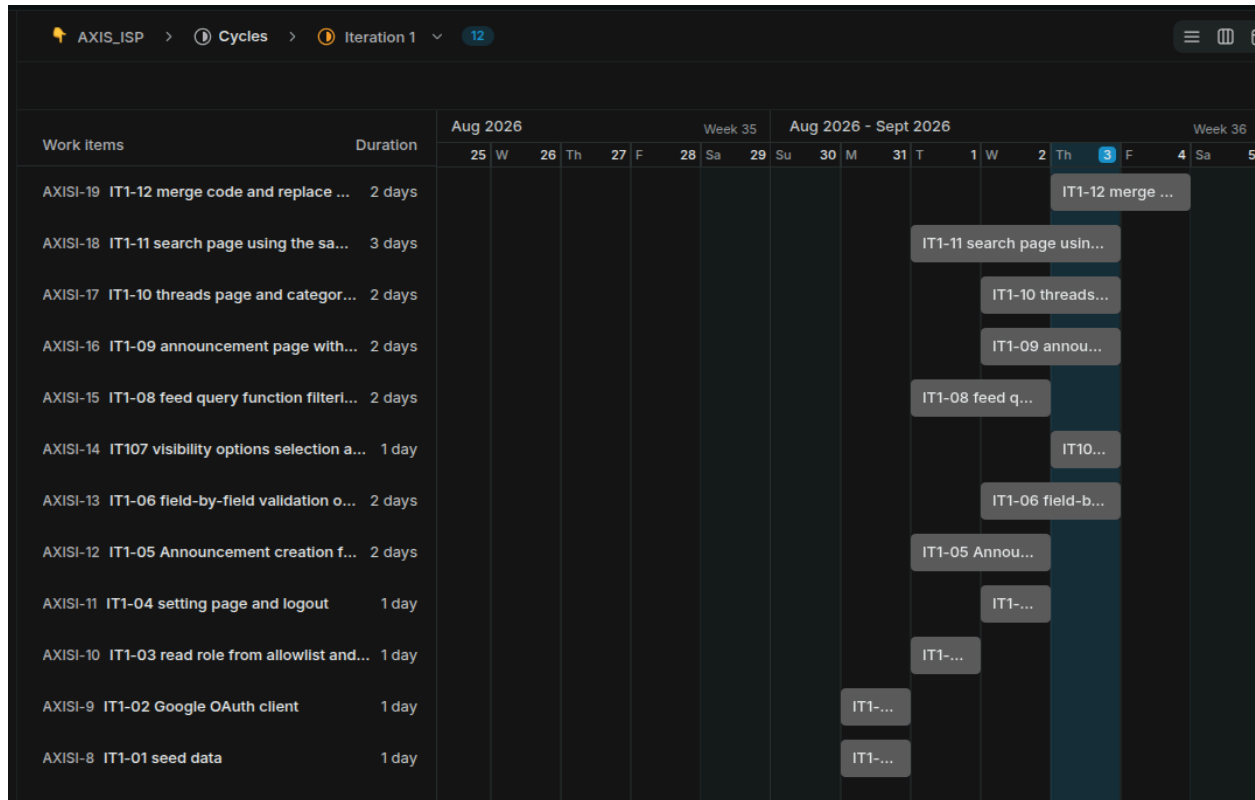

Critical Path: Database schema and seed data → Sign in with a university account (US-4) → Create and edit a content item (US-5) → Feed filtered by visibility (US-1)

The schema and its seed data were placed first so that the feed and the creation form could be built in parallel rather than in sequence. Without seeded items the feed story would have had to wait for the creation story to finish, which one week does not allow.

Critical Path Duration: 5 calendar days

2. Sprint/Board Status Snapshot

Iteration Goal: Deliver a working, demonstrable slice in which a member of the department can sign in with a university Google account, an authorised editor can create and edit a content item, and the feed shows only those items the signed-in account is permitted to see. This supports SG-1, SG-2, and SG-3 from the SRS.

Capacity Declared: three user stories, the fixed ceiling for a first iteration. No velocity baseline exists yet, so the ceiling was accepted rather than argued.

User Story	Description	Owner	Status	Within Capacity	Notes
US-4	As a member of the department, I want to sign in with my university Google account.	Piyatida Muanjaingam	Done	Y	Blocks US-5 and US-1 for role checks; both were developed against a temporary session until this landed
US-5	As an editor, I want to create and edit a content item so that students receive new department information.	Thanakorn Innok	Done	Y	File upload deferred to Iteration 2; images referenced by URL in this iteration
US-1	As a student, I want to see all currently published department information in one feed so that I do not have to check several chat servers.	Jehan Tohdeng	Done	Y	Includes the thread view in read-only form; adding follow-up posts deferred to Iteration 2

Work outside the three stories: Database schema, container configuration, seed data, keyword search, and the manual test pass were carried out as supporting work rather than as a fourth user story, so that the declared capacity was not exceeded.

3. Scope Addition/Change Log

Item added or changed	Reason	What was dropped to compensate
(None applicable)	Team stayed within the originally committed 3 user stories for the full iteration	(None)

4. Retrospective

What went well	What did not go well	Action items for next iteration
All three committed user stories were delivered and the integrated build passed the manual test pass on the first run, including the checks that prove restricted items stay hidden from a visitor who is not signed in	Environment setup consumed time on problems outside the code: a database container clashed with one left running by an unrelated project, and a machine ran out of disk space mid-task	Record the troubleshooting steps in the README and state a minimum free-disk requirement for development machines
Seeding the database with items covering all five content types on the first day let the feed and the creation form be built in parallel instead of in sequence, which is what made three stories fit into one week	A model name used during the feasibility work was withdrawn by its provider mid-test, breaking the whole script at once and costing an afternoon	Read model names from environment configuration and verify them with a live request rather than trusting a published list
—	Three stories in one week left no slack: the integration day had no room for a failure, and the team has no measured velocity to judge whether that pace holds	Record actual hours per story and use the result, rather than the ceiling, to set the capacity for Iteration 2

5. Testing & Quality Notes

Feasibility work completed before implementation: Extraction of structured fields from Thai announcement captions returned correct results in seven of eight samples. Buddhist-era years were converted correctly in every case, and a sample carrying no date returned no date rather than a guess. One sample took the name of the building hosting an event to be the target audience while reporting full confidence, which is the reason SRS-14 and SRS-15 place validation on the person rather than on any confidence value reported by an automated component. Embedding a public social media post rendered correctly without an application review. Open Graph metadata was present on the university site and absent on the department site, so manual entry of preview data is treated as the primary path rather than the exception.

Manual test pass for this iteration: A pass of twenty-two checks was written before the code was merged and run once the three stories were integrated. The checks are grouped by the behaviour each one proves rather than by the page it happens on, so that a check failing points at a rule rather than at a screen.

Every check passed on the first run. The checks that carry the most weight are the ones that prove a refusal rather than a result: an account outside the permitted domain is refused and no session is created; an item saved without a title or a department is refused and the missing field is named; and a visitor who is not signed in receives none of the restricted items, whether through the feed, through search, or by opening an item address directly. The last of these was tested three ways deliberately, because a rule that holds on one page and not another is the failure this system is most exposed to.

No defects were recorded during the pass. Two limitations are known and were accepted rather than fixed: file upload is not implemented, so posters are referenced by URL in this iteration, and follow-up posts in a thread can be seeded but not added through the interface. Both are carried into Iteration 2 rather than logged as defects, since neither was within the committed scope.

6. Project Risk Register

ID	Description	L	I	Mitigation / Contingency	Status
R-01	Staff accounts may sit in a different email domain from student accounts, in which case the domain restriction in SRS-10 excludes staff from the system entirely. The correction lies in the identity provider configuration rather than in this system, so it cannot be fixed late	H	H	Confirm the domain with the stakeholder before Iteration 2 and allow the permitted-domain setting to accept more than one value	Open
R-02	The team has no velocity baseline, so the self-declared capacity for later iterations may be miscalibrated once the fixed ceiling lifts	H	M	Record actual time spent per story in this iteration and compare it against the estimate before declaring the next capacity	Open
R-03	Features that depend on services outside the team's control may stop working from a policy change or a withdrawn model, which happened once already during feasibility testing	H	M	Every assisted path has a manual fallback, and each of these features can be removed without affecting the core system	Monitoring
R-04	Target audience is assigned by hand, so an item tagged for the wrong department or year reaches the wrong students with no signal that anything went wrong	M	H	Restrict tagging to authorised editors and refuse to save an item whose target audience is missing	Open
R-05	Knowledge of the container setup and deployment is concentrated in one member	M	H	Record the setup steps in the README and have a second member rebuild the environment from those steps alone during Iteration 2	Open

7. Individual Contribution Log

Student Name	Tasks owned this sprint	Course concept(s) applied	Evidence	Self-rated effort (1-5)
Piyatida Muanjaingam	Authentication, domain restriction, role model, sign out (US-4)	Separation of authentication from authorisation, and the decision to place both in a cross-cutting module rather than in each page, from the architecture material	https://github.com/ratamon2606-create/AXIS/tree/feat/auth	4
Thanakorn Innok	Content model and the create and edit form (US-5)	Turning SRS-14 and SRS-15 into validation at the model layer so that a page added later cannot bypass it	https://github.com/ratamon2606-create/AXIS/tree/feat/content-form	4
Jehan Tohdeng	Feed, visibility rules, and the thread view (US-1)	Traceability from SRS-1 through to the query conditions actually written	https://github.com/ratamon2606-create/AXIS/tree/feat/feed-thread	4
Ratamon Charoenratanakun	Database schema, container configuration, seed data, search, manual test pass	Reproducible development environments, and the port and volume configuration that made a clash with another project a one-line fix	https://github.com/ratamon2606-create/AXIS/tree/feat/infra-search	3
